


Probability × Impact Matrix — Model Answer

Y-axis: Probability (P1=Rare, P5=Almost Certain) · X-axis: Impact (I1=Negligible, I5=Critical)

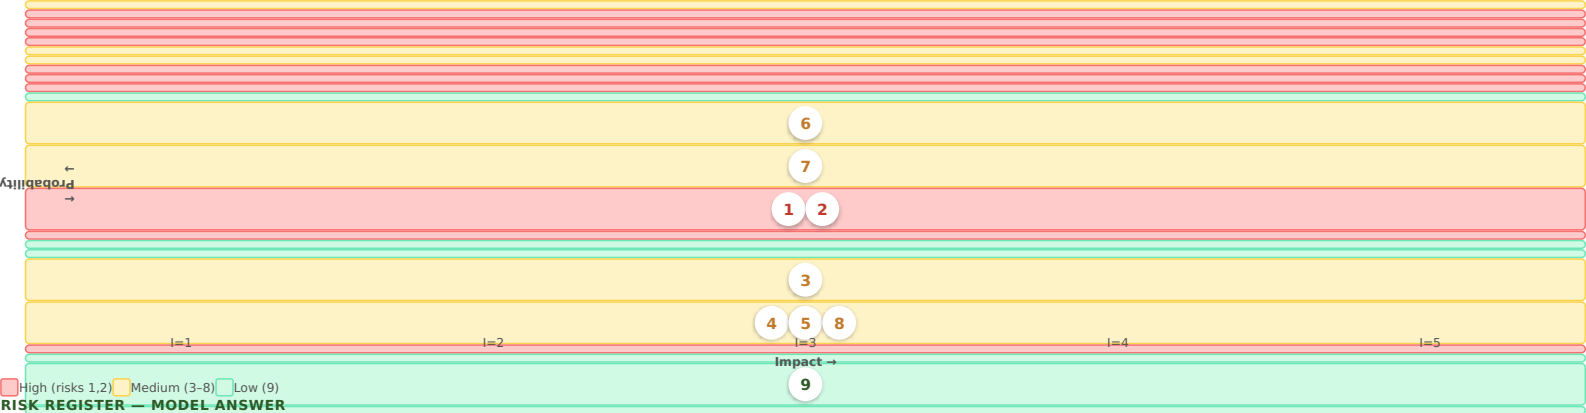

#	Risk	P	I	Rating	Mitigation
1	Staff resistance to digital (Mary, John)	3	4	High	Simplest interface; hands-on training before go-live; 2-week parallel run (paper + digital)
2	\$25K upfront cost strains \$4.1K/month surplus	3	4	High	Apply SME Go Digital grant; negotiate payment plan with vendor; defer Phase 2 if Phase 1 uplift insufficient
3	Customers refuse QR; revert to counter queue	2	3	Medium	Counter ordering remains as permanent fallback; QR is always opt-in — not mandatory
4	Vendor lock-in or poor local SaaS support	2	4	Medium	IMDA-approved vendor list; require SLA in contract; build data export capability from Day 1
5	Darren not ready to run AMK independently	2	4	Medium	6-month supervised preparation; formal milestone review before AMK opens; John remains on call
6	AMK Food Centre unit unavailable when ready	3	2	Medium	Begin AMK landlord conversation during Phase 1; identify backup location (AMK Hub as alternative)
7	Ingredient cost increases erode margin further	3	3	Medium	Phase 1 revenue uplift (8–10% projected) should offset; John to consider modest price adjustment in Year 2
8	Digital system downtime during peak hours	2	4	Medium	Require 99.9% uptime SLA; maintain paper backup process for first 3 months post-go-live
9	Customer data privacy concern with digital loyalty	1	2	Low	PDPA compliance built into vendor selection; clear opt-in for loyalty programme; no data sold
